


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Thu 05/12/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**60°F Overcast



**Wind:** 4 MPH S

**Precipitation:** .0"

**Humidity:** 95%

**12:00 PM:**68°F Overcast



**Wind:** 10 MPH W

**Precipitation:** .0"

**Humidity:** 77%

**4:00 PM:**72°F Partly Cloudy



**Wind:** 12 MPH W

**Precipitation:** .0"


**Humidity:** 58%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electrician working on Multiple tasks	1	8.0
Classic Touch Painting	Paint Ceilings- Main Entrance Lobby & Open office Building Dept. Prep Stairwell for Painting. Paint / prepare wood trim samples for Architect review.	1	8.0
Dumex Construction	Drywall Install - Four man Crew. Drywall taping - 1 Taper.	5	8.0
e.Norman Security	Install / Pull wire for Security System.	2	8.0
Midwest Mechanical	HVAC Duct work install - RFI 10 Service Tech- Review Job - for unit start -ups- Evaluation on Existing HVAC equipmnt.	2	8.0
Team Logic IT	Install Cable for Voice & Data.	2	8.0
Troop Contracting	Jobsite Supervision	1	10.0
<b>Total</b>		<b>14</b>	<b>114.0</b>

## Notes, Issues, Concerns

1. Drywall taping

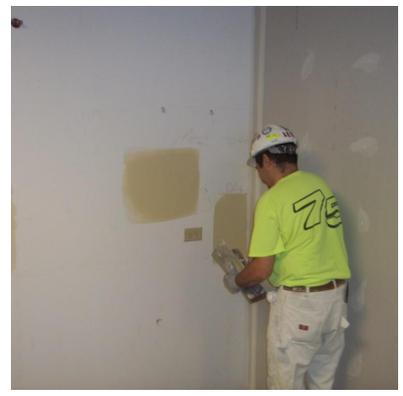


2. Low Voltage cabling / wiring - Security, Voice , & Data.



3. Painters Activities



4. Electrician activities

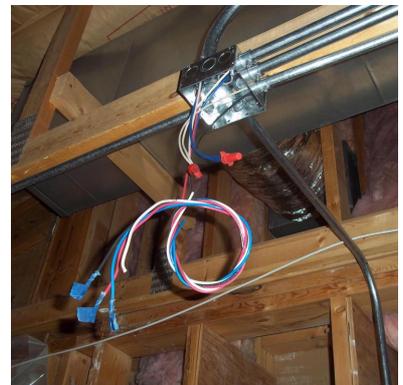

**Site Safety Observations**

No entry

**Quality Control Observations**

1. Weather - Humidity, - issue with the Drywall taping compound not drying- HVAC Contractor - re- starting Air Conditioning Equipment, to get building under a controlled / condition environment, for finishes.

## Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues
Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Install Of New exterior windows, Humidity, Not allowing drywall taping compound to dry fast enough.
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village of Homer Glen, Chief Building Official, Joseph Baber - Village of Homer Glen, Facility Manager, John Robinson meeting on site with Comcast.
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



---

I, Dave Bender, verify this report is accurate and complete.
