


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 03/21/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM: 30°F Clear
Wind: 3 MPH NE
Precipitation: .0"
Humidity: 80%



12:00 PM: 43°F Clear
Wind: 3 MPH NE
Precipitation: .0"
Humidity: 53%



4:00 PM: 51°F Mostly Cloudy
Wind: 7 MPH NE
Precipitation: .0"
Humidity: 42%




Work Logs

Name	Description	Quantity	Hours
Arc Electric	Rough in Electric - New work	1	8.0
Dumex Construction	Metal stud framing new work. Drywall tapers - skim coat walls were wall paper removed.	5	8.0
Prime Scaffolding	Erect shoring scaffold for support, column removal.	3	8.0
Stutz Plumbing	Rough in plumbing - new work	2	8.0
Valley Fire Protection	Removed and capped - fire suppression lines in conflict with Steel erection	1	6.0
Total		12	94.0

Notes, Issues, Concerns

1. Drywall Tapers skim coat walls, after wall paper removal

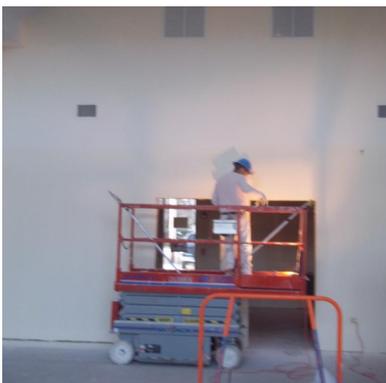

2. Prime Scaffolding - set shoring to support wood beams



3. Metal Stud Framing of New Offices



Site Safety Observations


No entry

Quality Control Observations

1.

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Approved Submittals
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Village of Homer Glen Office personal
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A

A handwritten signature in black ink, consisting of several loops and a long horizontal stroke extending to the right.

I, Dave Bender, verify this report is accurate and complete.
