


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 03/23/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM: 40°F Overcast
Wind: 10 MPH NE
Precipitation: .0"
Humidity: 84%



12:00 PM: 48°F Partly Cloudy
Wind: 9 MPH NE
Precipitation: .0"
Humidity: 72%



4:00 PM: 49°F Drizzle
Wind: 11 MPH NE
Precipitation: .01"
Humidity: 75%



Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric rough in for new lighting in offices	2	8.0
Dumex Construction	Framed header at stair ST2-1 Framed openings for new windows at office 170.	3	8.0
Jam Graphics	Installation of Project Sign	2	3.0
Midwest Mechanical	HVAC Duct work install.	2	8.0
Prime Scaffolding	Finished shoring wood beams for demolition.	3	8.0
Stutz Plumbing	Plumbing rough in for community & Sheriff kitchen areas. Concrete in floor after underground inspection.	2	8.0
Total		14	102.0

Notes, Issues, Concerns


1. Shoring complete for beam demolition



2. Project Sign Installed



3. Plumbing inspection

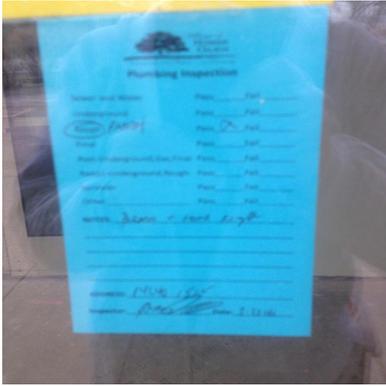

4. New Header Framed



5. New Duct Work Installed



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Responses to HVAC RFI's Re Submittals for approvals
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	e.Norman Security - reviewed Security drawings and Door Schedule.
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	HVAC - Installation is falling behind Schedule.
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A



I, Dave Bender, verify this report is accurate and complete.
