


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 03/24/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM: 42°F Light Rain



Wind: 5 MPH N

Precipitation: .01"

Humidity: 96%

12:00 PM: 49°F Heavy Rain



Wind: 7 MPH NE

Precipitation: .27"

Humidity: 95%

4:00 PM: 44°F Light Rain



Wind: 12 MPH NE

Precipitation: .02"


Humidity: 89%

Work Logs

Name	Description	Quantity	Hours
Dumex Construction	Frame offices at Sheriffs Dept Area.	3	8.0
Prime Scaffolding	Additional shoring in basement to support precast floor for Structural Steel Erection.	2	8.0
Safe Environmental	Demolition of wood beam column.	2	8.0
Stutz Plumbing	Concrete infill underground plumbing	2	8.0
Total		9	72.0

Notes, Issues, Concerns

1. Demolition of Main Wood Beam Column

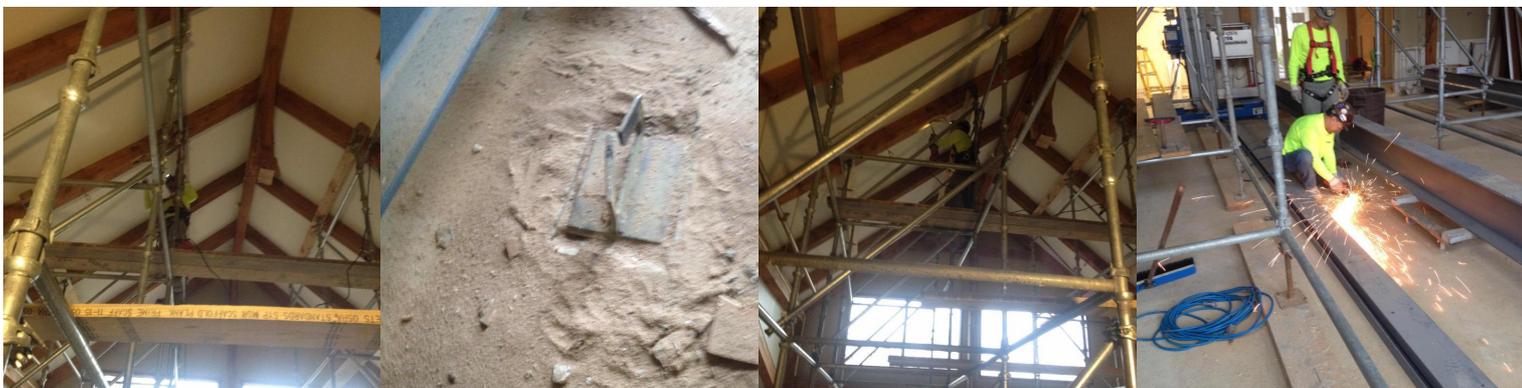

2. Plumbers concrete in filled under ground



3. Shoring in basement to support Structural Steel Erection Activity



4. Wall framing Sheriff's Department Officed



5. Double Doors Water Leak



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole shoring braces for hollow core panels



I, Dave Bender, verify this report is accurate and complete.
