


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 03/30/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:42°F Mostly Cloudy



Wind: 8 MPH NE
Precipitation: .0"
Humidity: 66%

12:00 PM:51°F Overcast



Wind: 13 MPH NE
Precipitation: .0"
Humidity: 56%

4:00 PM:61°F Mostly Cloudy



Wind: 17 MPH NE
Precipitation: .0"
Humidity: 65%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough in Power Circuits For New Sump Pump	1	8.0
Kure Steel Erector set	Steel Erection Board Room & Community Room	5	8.0
Midwest Mechanical	Install HVAC Duct Work	1	8.0
Straight Line Concrete Cutting	Saw Cut Concrete Slab in Basement For New Sump Pit.	1	2.0
Stutz Plumbing	Install New Sump Pit & Pump in Mechanical Room 010	2	8.0
Total		10	74.0

Notes, Issues, Concerns

1. Concrete Slab Cutting For New Sump Pit




2. Steel Erection at Board Room & Community Room



3. HVAC Duct Work Install



4. Sump Pump Install

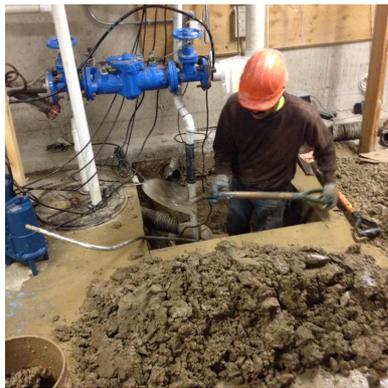

5. Electric Circuit for New Sump Pumps



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	(OAC) - Owner, Architect, & Contractor, Weekly Meeting #3
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces & Shoring Equipment for Structural Steel Erection.



I, Dave Bender, verify this report is accurate and complete.
