


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 04/08/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:35°F Mostly Cloudy



Wind: 3 MPH SW
Precipitation: .0"
Humidity: 83%

12:00 PM:41°F Light Rain



Wind: 17 MPH W
Precipitation: .01"
Humidity: 72%

4:00 PM:48°F Breezy and Overcast





Wind: 18 MPH NW
Precipitation: .0"
Humidity: 65%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough in. 3" Conduit for Generator- core hole, start running pipe.	2	6.0
Dumex Construction	Frame work for New Exterior Windows. Layout & wall construction in Board Room.	2	8.0
Midwest Mechanical	HVAC Duct work install. Install Refrigerant Lines / Line sets for New Unit.	1	8.0
Troop Contracting	Job Site Supervision	1	8.0
Total		6	44.0

Notes, Issues, Concerns

1. Electric Rough In.
Core drill for 3" conduit to Generator

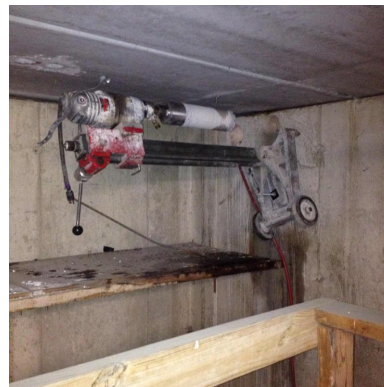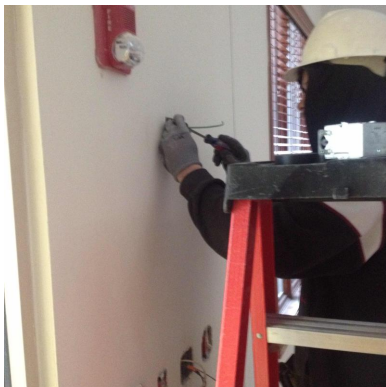

2. HVAC Duct Work.
Refrigerant Lines / Line sets installed for New Units.



3. Exterior Window Framing.
Wall Framing.



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues
Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Rain / Snow - Delay Concrete pad for Generator.
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	BA From Bricklayers- stopped by.
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Pole Braces & Shoring Equipment for Structural Steel Erection.

A handwritten signature in black ink, appearing to be 'D.B.K.', located in the upper right corner of the page.

I, Dave Bender, verify this report is accurate and complete.
