


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Report Date** 04/11/2016

**Job Number** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**46°F Overcast



**Wind:** 5 MPH SW  
**Precipitation:** .0"  
**Humidity:** 95%

**12:00 PM:**47°F Partly Cloudy



**Wind:** 16 MPH W  
**Precipitation:** .0"  
**Humidity:** 60%

**4:00 PM:**50°F Partly Cloudy



**Wind:** 16 MPH NW  
**Precipitation:** .0"  
**Humidity:** 45%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Installing 3" conduit for Generator	2	8.0
Dumex Construction	Layout Walls. Construct New Walls in Board Room. Drywall Infills.	2	8.0
Heartland Cabinetry	Field Measure for Wood Base, & Chair Rail.	1	8.0
Troop Contracting	Job Site Supervision.	1	10.0
<b>Total</b>		<b>6</b>	<b>50.0</b>

## Notes, Issues, Concerns


1. Metal Stud Wall Framing.  
Drywall Infills.



2. 3" conduits for Generator



### 3. Field Measure Steel for Wood Wrap

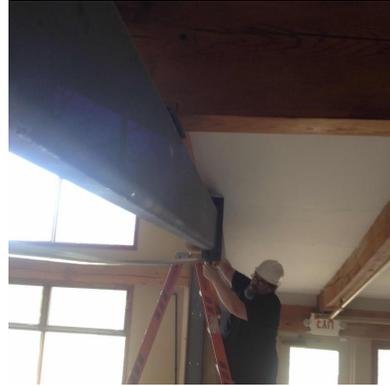

### Site Safety Observations

No entry

### Quality Control Observations

No entry

### Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material.- Answers on RFI's HVAC ,Outstanding. SIPS Panels - Roof Leaks.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Meeting - TRIA Architecture, Heartland Cabinetry & Troop Contracting, on Structural Steel Wood Raping, & The Barn Door, Issues.
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces & Shoring Equipment for Structural Steel Erection.



---

I, Dave Bender, verify this report is accurate and complete.
