


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 04/12/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:31°F Clear



Wind: 3 MPH NW
Precipitation: .0"
Humidity: 72%

12:00 PM:45°F Clear



Wind: 4 MPH NW
Precipitation: .0"
Humidity: 41%

4:00 PM:49°F Clear




Wind: 5 MPH NE
Precipitation: .0"
Humidity: 40%

Work Logs


Name	Description	Quantity	Hours
Dumex Construction	Metal Stud Framing For Wall in back of DAIS 150. Drywall patch Infills.	2	8.0
Midwest Mechanical	Soldered Copper Line sets for New HVAC Equipment.	1	4.0
Troop Contracting	Job Site Supervision	1	8.0
Total		4	28.0

Notes, Issues, Concerns

1. Metal Stud Wall Framing

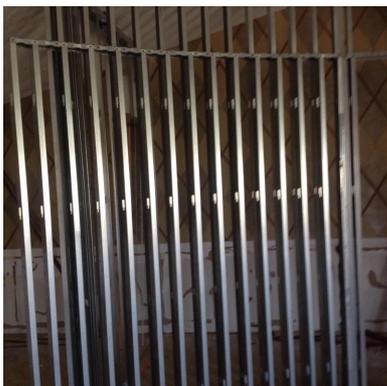

2. Copper line Sets Soldered

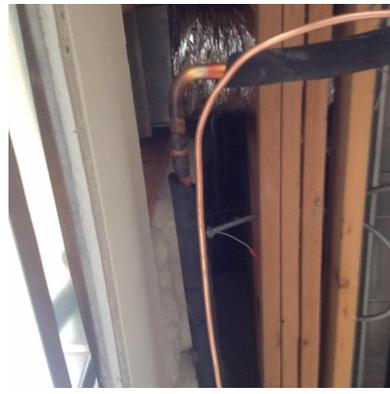

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material. - SIPS panels Issues - HVAC RFI Responses.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Superintendent from Modernfold Chicago - Site Visit. Village Of Homer Glen - John Robinson & Joseph Baber - Walk Trough.
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Pole Braces & Shoring Equipment for Structural Steel Erection.

I, Dave Bender, verify this report is accurate and complete.
