


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Report Date** 04/13/2016

**Job Number** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**35°F Clear



**Wind:** 3 MPH E  
**Precipitation:** .0"  
**Humidity:** 72%

**12:00 PM:**54°F Clear



**Wind:** 6 MPH SE  
**Precipitation:** .0"  
**Humidity:** 47%

**4:00 PM:**60°F Clear




**Wind:** 8 MPH SE  
**Precipitation:** .0"  
**Humidity:** 40%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Rough in electric boxes & conduit @ new walls.	2	8.0
Midwest Mechanical	Finish soldering copper line sets for New HVAC Equipment.	1	0.0
Troop Contracting	Jobsite Supervision	1	11.0
<b>Total</b>		<b>4</b>	<b>27.0</b>

## Notes, Issues, Concerns

### 1. Copper line sets soldered

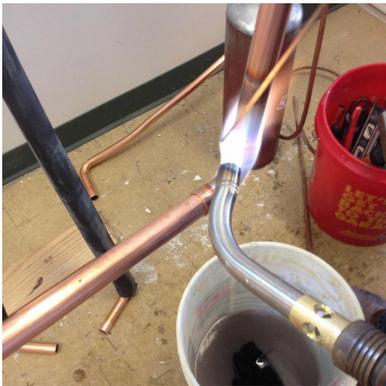

### 2. Electric Rough In



### Site Safety Observations

No entry

### Quality Control Observations

No entry

### Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material. - SIPS panels Issues - HVAC RFI Responses.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	OAC Meeting
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

I, Dave Bender, verify this report is accurate and complete.
