


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 04/18/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:53°F Clear



Wind: 2 MPH S
Precipitation: .0"
Humidity: 65%

12:00 PM:78°F Clear



Wind: 5 MPH SE
Precipitation: .0"
Humidity: 31%

4:00 PM:86°F Partly Cloudy



Wind: 7 MPH SE
Precipitation: .0"
Humidity: 25%

Work Logs


Name	Description	Quantity	Hours
Arc Electric	Electric rough in.	2	8.0
Midwest Mechanical	HVAC work	2	8.0
Superior Flooring	Patch holes in floor, install 1/4" Luan over floor.	1	8.0
Troop Contracting	Jobsite Supervision - Phone Work on tracking down a SIPS Contractor for Existing Roof Leak.	1	8.0
Total		6	48.0

Notes, Issues, Concerns

1. Electric Rough



2. HVAC Work

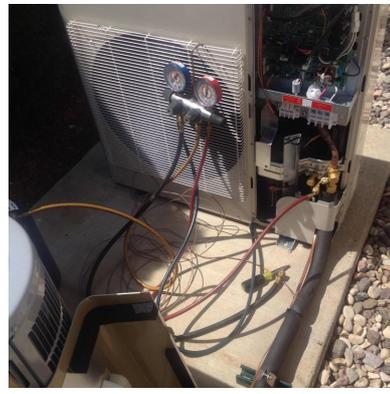

3. Floor Patching & Luan Install



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material. - SIPS panels Issues - HVAC RFI Responses.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Deputy Fire Marshal- Dave Brickert - On Fire Suppression & Fire Alarm - review Comments, Bid set Drawings, VS Actual Field Conditions.MR Duct- Jobsite walk through on Duct Cleaning Quote. Hunter Paving- Jobsite Visit for Asphalt repair to golf cart path.
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC Contractor - * In Review of

Any equipment rented on site?

Pole Braces to support Precast floor

I, Dave Bender, verify this report is accurate and complete.
