


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 04/19/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:50°F Partly Cloudy



Wind: 6 MPH NE
Precipitation: .0"
Humidity: 69%

12:00 PM:62°F Partly Cloudy



Wind: 8 MPH NE
Precipitation: .0"
Humidity: 55%

4:00 PM:73°F Overcast




Wind: 14 MPH NE
Precipitation: .0"
Humidity: 49%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough in for Security wiring.	2	8.0
Midwest Mechanical	HVAC Install	1	8.0
Superior Flooring	Laminate 1/4" Luan Board @ Sheriff's office Area.	1	8.0
Troop Contracting	Jobsite Supervision	1	10.0
Total		5	42.0

Notes, Issues, Concerns

1. Electric Rough in

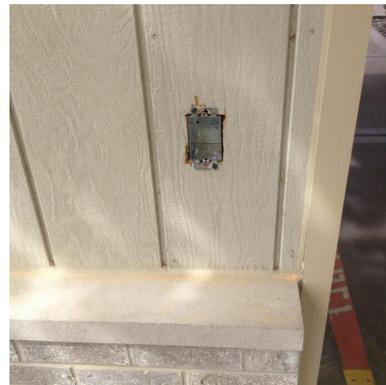

2. 1/4" Luan installed



3. HVAC UNIT



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material. - SIPS panels Issues - HVAC RFI Responses.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	J & L Door - Field Verify Existing Door frames- Pre-Door Order Release.
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC Contractor - * In Review of Architect, MEP Engineers, Comments on Outstanding RFI's.
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

DBA

I, Dave Bender, verify this report is accurate and complete.
