


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 04/21/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:57°F Mostly Cloudy



Wind: 4 MPH S

Precipitation: .0"

Humidity: 96%

12:00 PM:67°F Mostly Cloudy



Wind: 4 MPH W

Precipitation: .0"

Humidity: 60%

4:00 PM:70°F Light Rain



Wind: 4 MPH SW

Precipitation: .01"


Humidity: 52%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough continues	2	8.0
Midwest Mechanical	Natural Gas Pipe Install.	2	8.0
Troop Contracting	Jobsite Supervision	1	8.0
Total		5	40.0

Notes, Issues, Concerns

1. Electric Rough In

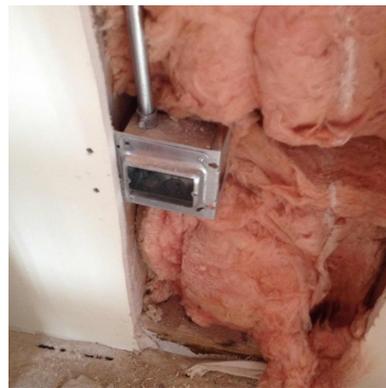

2. Natural Gas Pipe Install



3. Discovered Vapor Barrier and Insulation wet behind drywall opened up for TV back boxes at Conference Room 139



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues - Finalizing HVAC RFI's - Fire Marshal Review Comments, Submitted for Architect, Village review.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC Contractor - * In Review of Architect, MEP Engineers, Comments on Outstanding RFI's.
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

DRB

I, Dave Bender, verify this report is accurate and complete.
