


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Report Date 04/22/2016

Job Number 16-012

Prepared By Dave Bender

Weather

6:00 AM:51°F Partly Cloudy



Wind: 5 MPH NW
Precipitation: .0"
Humidity: 93%

12:00 PM:49°F Overcast



Wind: 13 MPH N
Precipitation: .0"
Humidity: 80%

4:00 PM:58°F Mostly Cloudy




Wind: 14 MPH N
Precipitation: .0"
Humidity: 68%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough In	2	8.0
Midwest Mechanical	Deliver gas pipe. Pump up gas lines for pressure test. Welding Gas Pipe.	2	8.0
Troop Contracting	Jobsite Supervision	1	8.0
Total		5	40.0

Notes, Issues, Concerns

1. Electric Rough

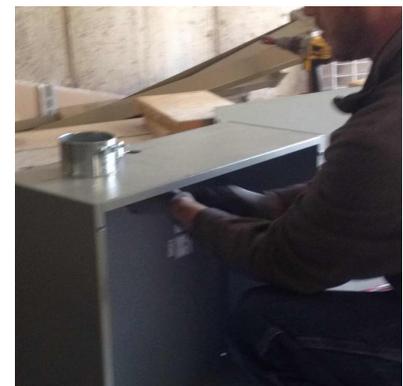

2. Pressure Test Gas Line



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues - Finalizing HVAC RFI's - Fire Marshal Review Comments, Submitted for Architect, Village review.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC Contractor - * In Review of Architect, MEP Engineers, Comments on Outstanding RFI's.
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

I, Dave Bender, verify this report is accurate and complete.
