


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Thu 04/28/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:45°F Overcast



Wind: 10 MPH NE
Precipitation: .0"
Humidity: 93%

12:00 PM:49°F Overcast



Wind: 6 MPH NE
Precipitation: .0"
Humidity: 90%

4:00 PM:51°F Overcast



Wind: 7 MPH NE
Precipitation: .0"
Humidity: 84%

Work Logs


Name	Description	Quantity	Hours
Arc Electric	Set New Panel MDPE outside wall IT Room 006. Install 3" conduit feeds to panel. Electric rough in.	2	8.0
Dumex Construction	Install Plywood, drywall & door frame @ South wall for IT room 006. Start Hollow Metal door frame install.	2	8.0
Midwest Mechanical	Complete 3" gas line for New Generator.	2	8.0
Troop Contracting	Jobsite Supervision	1	8.0
Total		7	56.0

Notes, Issues, Concerns

1. Panel install



2. 3" Gas Line

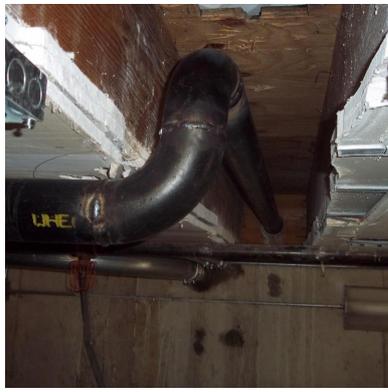

3. Door Frames



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues - Finalizing HVAC RFI's - Fire Marshal Review Comments, Submitted for Architect, Village review.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC Contractor - Waiting on MSK's & approvals from HVAC RFI's
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

A handwritten signature in black ink, appearing to be 'DB' or similar, located at the top right of the page.

I, Dave Bender, verify this report is accurate and complete.
