


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Sat 04/30/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**46°F Overcast



**Wind:** 7 MPH NE  
**Precipitation:** .0"  
**Humidity:** 89%

**12:00 PM:**47°F Light Rain



**Wind:** 13 MPH NE  
**Precipitation:** .05"  
**Humidity:** 90%

**4:00 PM:**46°F Rain





**Wind:** 12 MPH NE  
**Precipitation:** .07"  
**Humidity:** 94%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough In	2	8.0
Troop Contracting	SIPS Panel - Wall & Drywall Demolition	1	5.0
<b>Total</b>		<b>3</b>	<b>21.0</b>

## Notes, Issues, Concerns



### 1. Electric Rough In

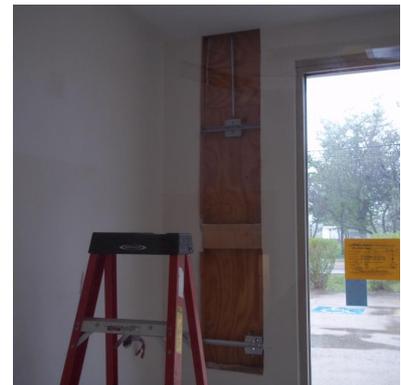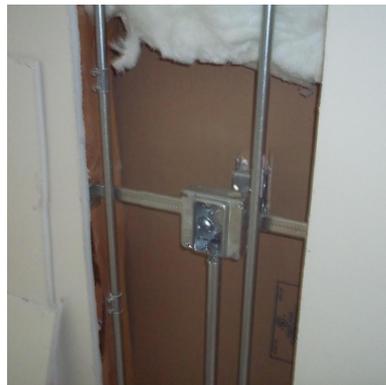

### 2. SIPS Panel Demolition - Sheriff's office 169



### 3. Basement Foundation Crack - Sheriff's Stairs

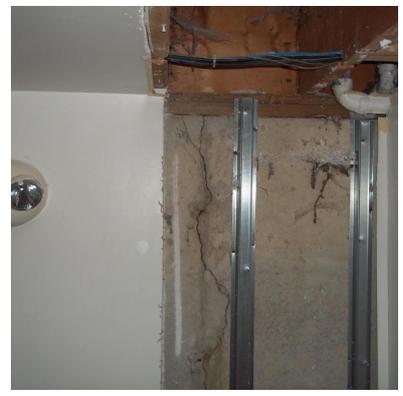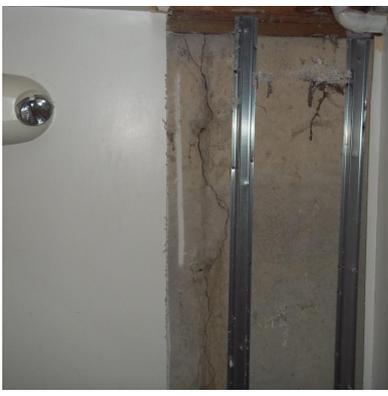

4. SIPS Panel Roof Leak - Board Room



**Site Safety Observations**

No entry

**Quality Control Observations**

No entry

**Survey**

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues - Finalizing HVAC RFI's - Fire Marshal Review Comments, Submitted for Architect, Village review.
Did weather cause any delays?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Rain - Delayed Shingle Removal - SIPS Panel Leaks
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC RFI's- To Complete Duct Work Install. - Board Room & Community Rooms, due To SIPS Panels water Leaks.
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

A handwritten signature in black ink, consisting of several loops and a final horizontal stroke.

---

I, Dave Bender, verify this report is accurate and complete.
