


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Wed 05/04/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**48°F Light Rain



**Wind:** 8 MPH N  
**Precipitation:** .01"  
**Humidity:** 91%

**12:00 PM:**51°F Mostly Cloudy



**Wind:** 13 MPH N  
**Precipitation:** .0"  
**Humidity:** 62%

**4:00 PM:**51°F Overcast



**Wind:** 14 MPH NW  
**Precipitation:** .0"  
**Humidity:** 59%

## Work Logs


Name	Description	Quantity	Hours
Arc Electric	Rough in for lighting. Rough in for security wiring.	2	8.0
Dumex Construction	Install hollow metal door & window frames Start Drywall install	4	8.0
Midwest Mechanical	Field review of MSK's Just Recived From Mechanical Engineer. Misc- Work.	2	8.0
Troop Contracting	Jobsite Supervision	1	12.0
<b>Total</b>		<b>9</b>	<b>76.0</b>

## Notes, Issues, Concerns


### 1. Hollow Metal Frame Install



### 2. 1st Day- Drywall Install.

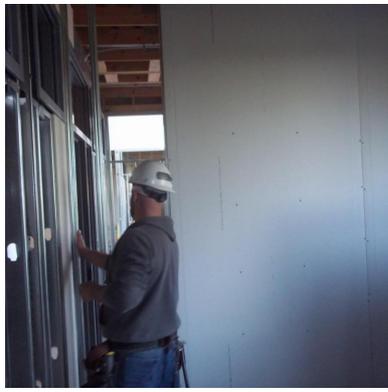

**3. Electric Rough In- Lighting**

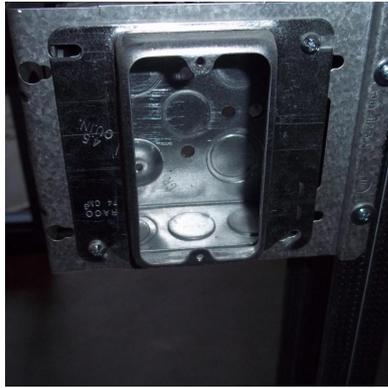

**4. Demolition of Drywall Ceiling at Sheriff's Area - To install HVAC duct Work - per MSK # 6 & # 7.**



**Site Safety Observations**

No entry

**Quality Control Observations**

No entry

**Survey**

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Issues - Finalizing HVAC

Did weather cause any delays?

N/A

Any visitors on site?

Ceiling Demo for HVAC, Wet Insulation & drywall- discovered.- CWSC Field Measure for New Office Furniture. 5 Star Decorating - walk thru job for painting re- quote. OAC Weekly Meeting. .

Any areas that can't be worked on?

Board Room& Community Room - Due to SIPS Panel Issues.

Any equipment rented on site?

Pole Braces to support Precast floor



---

I, Dave Bender, verify this report is accurate and complete.
