


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Wed 05/11/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**57°F Foggy

 **Wind:** 2 MPH NE  
**Precipitation:** .0"  
**Humidity:** 97%

**12:00 PM:**67°F Mostly Cloudy

 **Wind:** 5 MPH E  
**Precipitation:** .0"  
**Humidity:** 79%

**4:00 PM:**78°F Partly Cloudy

 **Wind:** 7 MPH SE  
**Precipitation:** .0"  
**Humidity:** 66%

## Work Logs

| Name                   | Description  | Quantity  | Hours       |
|------------------------|--|-----------|-------------|
| Arc Electric           | Electric work  | 2         | 8.0         |
| Classic Touch Painting | Painted ceilings in main Entrance Foyer & Open offices Building Dept.<br>Stains samples - for re-review. | 1         | 8.0         |
| Dumex Construction     | Drywall Install & Taping. - 4 Rockers, 1 Taper   | 5         | 8.0         |
| e.Norman Security      | Install / pull- Security Wiring  | 2         | 8.0         |
| Team Logic IT          | Install / pull - Data & Voice wiring   | 2         | 0.0         |
| Troop Contracting      | Jobsite Supervision  | 1         | 11.0        |
| <b>Total</b>           |  | <b>13</b> | <b>91.0</b> |

## Notes, Issues, Concerns

### 1. Drywall Install



### 2. Drywall taping




3. Drywall taping



4. Low voltage wire install



5. Stain samples for re- submit

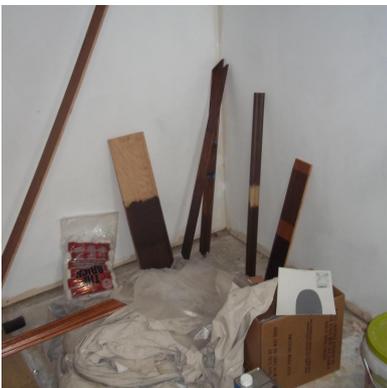

6. Stain samples for re- submit



## Site Safety Observations

---

No entry

## Quality Control Observations

---

No entry

## Survey

---

|                                      | No                                  | Yes                                 | Description  |
|--------------------------------------|-------------------------------------|-------------------------------------|--|
| Any accidents on site today?         | <input checked="" type="checkbox"/> | <input type="checkbox"/>            | N/A  |
| Hot issues that may effect schedule? | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | SIPS Panel Issues - Finalizing HVAC RFI's - Fire Marshal Review Comments, Submitted for Architect, Village review. |
| Did weather cause any delays?        | <input checked="" type="checkbox"/> | <input type="checkbox"/>            | N/A  |
| Any visitors on site?                | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | OAC Weekly Meeting   |
| Any areas that can't be worked on?   | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | Board room & Community Rooms - SIPS Panel Roof   |
| Any equipment rented on site?        | <input type="checkbox"/>            | <input checked="" type="checkbox"/> | Pole Braces to support Precast floor   |

---

I, Dave Bender, verify this report is accurate and complete.
