


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Mon 05/16/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:44°F Clear



Wind: 7 MPH S
Precipitation: .0"
Humidity: 72%

12:00 PM:66°F Partly Cloudy



Wind: 14 MPH SW
Precipitation: .0"
Humidity: 41%

4:00 PM:69°F Mostly Cloudy




Wind: 12 MPH SW
Precipitation: .0"
Humidity: 38%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Work	2	8.0
Classic Touch Painting	Paint Stairwell	1	8.0
Dumex Construction	Drywall install Drywall taping	4	8.0
e.Norman Security	Security Wiring	1	8.0
Midwest Mechanical	Re- Start existing HVAC equipment	2	8.0
Troop Contracting	Job Site Supervision	1	8.0
Total		11	88.0

Notes, Issues, Concerns



1. Drywall Taping

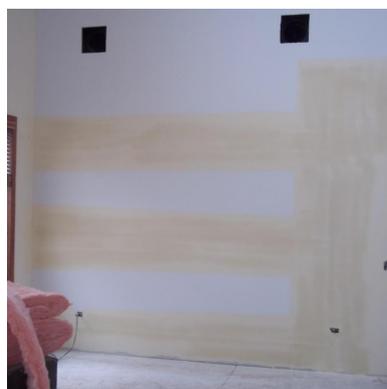

2. Layout for Concrete Slab cut - install floor boxes & Stub up Feeds to Conf Room Tables



3. Stairwell Painted

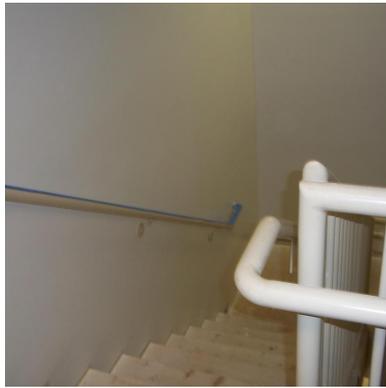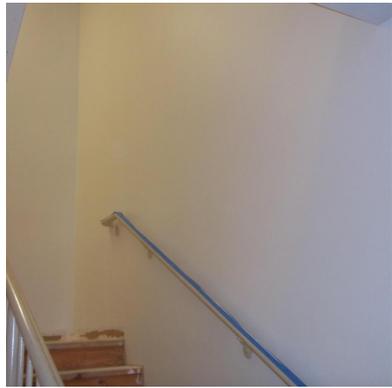

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Roof Leak - Received ASK's for Repair on 5-13-16, Troop Contracting in review of ASK's, to Prepare cost estimate.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

A handwritten signature in black ink, appearing to be 'DBH' with a stylized flourish at the end.

I, Dave Bender, verify this report is accurate and complete.
