


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 05/17/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:52°F Partly Cloudy



Wind: 4 MPH SW
Precipitation: .0"
Humidity: 80%

12:00 PM:60°F Mostly Cloudy



Wind: 8 MPH N
Precipitation: .0"
Humidity: 64%

4:00 PM:61°F Mostly Cloudy



Wind: 13 MPH N
Precipitation: .0"
Humidity: 55%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electrical Work	2	8.0
Classic Touch Painting	Paint / Stain For Mock ups - Owner, Architect, Approval. Prime Walls.	1	8.0
Cobra Concrete Cutting	Scanned Concrete slab and Hollow core. Saw Cut Concrete Slab & Hollow Core for Floor boxes.	1	8.0
Dumex Construction	2- Carpenters, Build stairs, ST2-1	5	8.0
Midwest Mechanical	Re- Start Existing HVAC Equipment. HVAC Duct Work install.	2	8.0
Troop Contracting	Job Site Supervision	1	8.0
Total		12	96.0

Notes, Issues, Concerns


1. Drywall Taping



2. Concrete Cutting



3. Drywall - Wall Priming

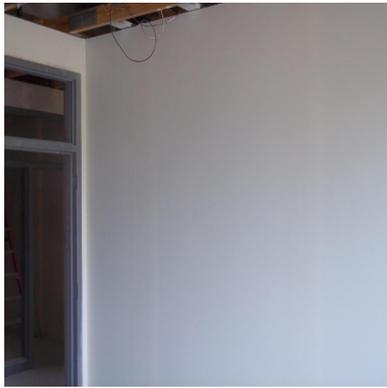


4. Mock - Ups, for Approval



5. Existing HVAC Equipment - Re Start up



6. ST2-1 Stairs

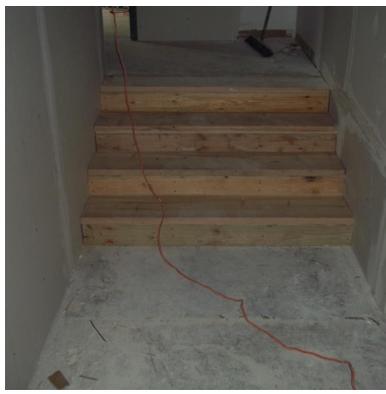

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Roof Leak - Received ASK's for Repair Work today, Troop Contracting in review of ASK's, to Prepare cost estimate.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village of Homer Glen, Chief Building Official, Joseph Baber
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

I, Dave Bender, verify this report is accurate and complete.
