


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Wed 05/18/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:42°F Partly Cloudy



Wind: 3 MPH N
Precipitation: .0"
Humidity: 75%

12:00 PM:60°F Clear



Wind: 5 MPH NE
Precipitation: .0"
Humidity: 52%

4:00 PM:67°F Partly Cloudy




Wind: 6 MPH NE
Precipitation: .0"
Humidity: 44%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electrical Work	2	8.0
Classic Touch Painting	Prime Walls	1	8.0
Dumex Construction	3 tapers - drywall taping. 2 Carpenters - install drywall, & rock wool insulation	5	8.0
Midwest Mechanical	Re-start Existing Equipment. Install duct work.	2	8.0
Troop Contracting	Job Site Supervision	1	10.0
Total		11	90.0

Notes, Issues, Concerns

1. Electric, Data, & Voice Feeds To Conference Room Tables.

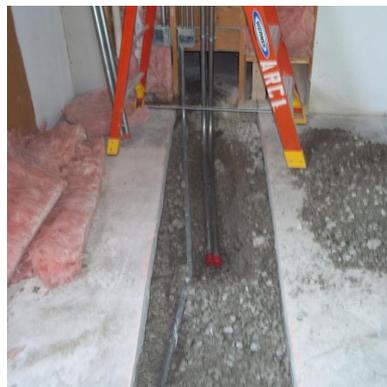

2. Drywall Taping




3. HVAC - Duct work install



4. HVAC Equipment - Survey & Re-start



5. Rock wool Sound Insulation, Install for Mayor's Office

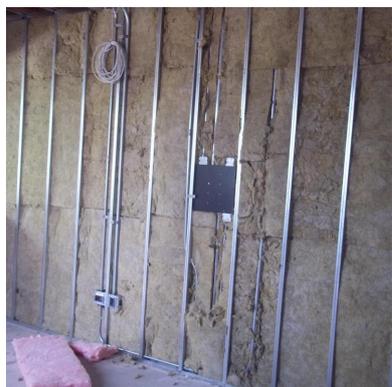

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel System - Water Leak
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Meeting- Tria Architecture, A/V Contractor, Electrician, & Troop Contracting, To discuss Layout and install for Board Room / Community Room. Weekly OAC Meeting
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board Room / Community Room - SIPS Panel Issues
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



I, Dave Bender, verify this report is accurate and complete.
