


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Mon 05/23/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:51°F Clear



Wind: 2 MPH S
Precipitation: .0"
Humidity: 78%

12:00 PM:77°F Clear



Wind: 7 MPH SE
Precipitation: .0"
Humidity: 34%

4:00 PM:85°F Clear



Wind: 9 MPH SE
Precipitation: .0"
Humidity: 27%

Work Logs



Name	Description	Quantity	Hours
Arc Electric	Electric Work	2	8.0
Classic Touch Painting	Prime, Prep walls & Wood Trim, Make ready for Paint	3	8.0
Dumex Construction	1 Carpenter, 2 drywall Tapers Finish Misc drywall install. Tapers continued Tapping / coating Walls	3	8.0
Heartland Cabinetry	Wood Trim Install	2	8.0
Midwest Mechanical	Start up New Equipment. Duct Work Take Off- RFI's	3	8.0
Troop Contracting	Job Site Supervision	1	8.0
Total		14	112.0

Notes, Issues, Concerns

1. Wood Trim Install




2. Prep work for painting

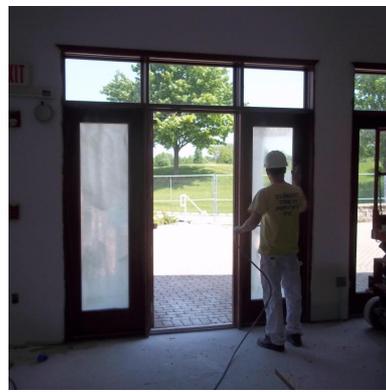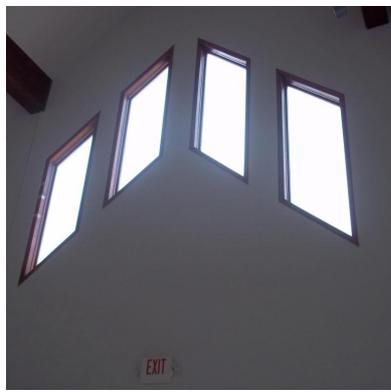

3. Drywall Install



4. Drywall Taping

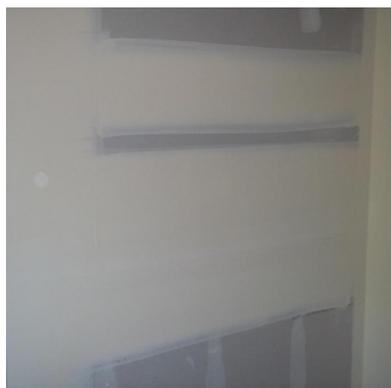

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel Roof Leak - Received ASK's for Repair Work, Troop Contracting in review of ASK's, to Prepare cost estimate.

Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Ni Core Gas Representative, Chief Building Official Joseph Baber - To Review Current Gas Meter - Gas Pressure to Building
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



I, Dave Bender, verify this report is accurate and complete.
