


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 05/24/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:59°F Clear



Wind: 4 MPH S
Precipitation: .0"
Humidity: 66%

12:00 PM:80°F Clear



Wind: 11 MPH S
Precipitation: .0"
Humidity: 40%

4:00 PM:88°F Clear





Wind: 13 MPH S
Precipitation: .0"
Humidity: 33%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Work	1	8.0
Classic Touch Painting	Prep, & Prime windows and Trim	2	8.0
Dumex Construction	1- Carpenter - Install Hanging wire for ceiling grid. 2- Drywall Tapers - Sanding, Skim Coating , Taping, & patching.	3	8.0
Heartland Cabinetry	Install Wood Trim Casing to New Hollow Metal Door & window Frames. Install Wood Chair rail in Corridors.	2	8.0
Midwest Mechanical	Install HVAC Duct	2	8.0
Troop Contracting	Job Site Supervision	1	8.0
Total		11	88.0

Notes, Issues, Concerns

1. Prep & Prime Widows & Wood Trim.

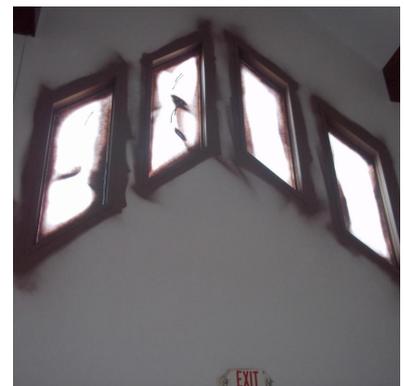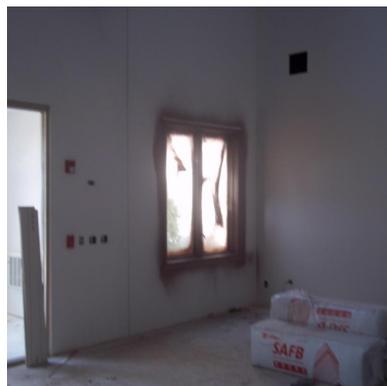

2. Drywall - Sanding, Taping



3. Install Hanger Wire for acoustic Ceiling



4. HVAC Duct Work Install



5. Install Wood Trim Hollow Metal Frames



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel System - Water Leak
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor - Scissors Lift Painting Contractor



I, Dave Bender, verify this report is accurate and complete.
