


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Thu 05/26/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:67°F Clear



Wind: 5 MPH S
Precipitation: .0"
Humidity: 90%

12:00 PM:77°F Mostly Cloudy



Wind: 11 MPH S
Precipitation: .0"
Humidity: 74%

4:00 PM:87°F Clear




Wind: 10 MPH SW
Precipitation: .0"
Humidity: 57%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Work - trim out panels	1	8.0
Classic Touch Painting	Paint- public washrooms, Paint walls Main Entrance Lobby,	3	8.0
Dumex Construction	2- Carpenters 2- Drywall Tapers. Misc Carpentry work. Start Ceiling Grid install. Tapers continue coating walls, Patching, & Skim Coating.	4	8.0
Heartland Cabinetry	Field Measuring- for Wood Steel wraps	2	6.0
Midwest Mechanical	Duct Work Install - office area	1	6.0
MR Duct	Clean all Existing HVAC Duct Work	7	8.0
Quinlan Security	Finished wiring for Fire Alarm added devices.	1	2.0
Troop Contracting	Job Site Supervision	1	12.0
Total		20	152.0

Notes, Issues, Concerns

1. HVAC Duct Cleaning

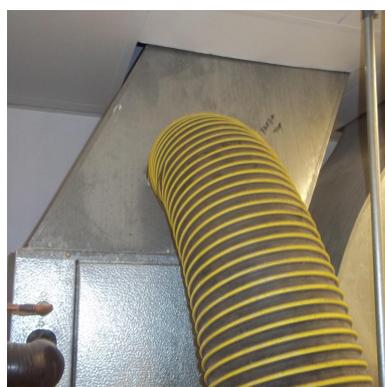

2. HVAC Duct Cleaning



3. Ceiling Grid Install



4. Drywall Taping



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	SIPS Panel System - Water Leak
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A

- | | | | |
|------------------------------------|--------------------------|-------------------------------------|--|
| Any visitors on site? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | Interior Designer, From Tria Architecture meet With Furniture Supplier on site to Field Measure. |
| Any areas that can't be worked on? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | Board room & Community Rooms - SIPS Panel Roof |
| Any equipment rented on site? | <input type="checkbox"/> | <input checked="" type="checkbox"/> | Pole Braces to support Precast floor - Scissors Lift Painting Contractor |



I, Dave Bender, verify this report is accurate and complete.
