


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Thu 06/02/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**59°F Clear



**Wind:** 2 MPH W  
**Precipitation:** .0"  
**Humidity:** 89%

**12:00 PM:**77°F Clear



**Wind:** 8 MPH W  
**Precipitation:** .0"  
**Humidity:** 44%

**4:00 PM:**80°F Clear



**Wind:** 8 MPH W  
**Precipitation:** .0"  
**Humidity:** 37%

## Work Logs


Name	Description	Quantity	Hours
Arc Electric	Electric Work	1	8.0
Classic Touch Painting	Prep, prime & Paint	2	8.0
Dumex Construction	2 Carpenters - Install Ceiling Grid. 2 Drywall Tapers - Taping, Coating	4	8.0
Heartland Cabinetry	Wood Trim Install	2	8.0
Midwest Mechanical	HVAC Duct Work Install	2	8.0
Troop Contracting	Job Site Supervision	1	9.0
<b>Total</b>		<b>12</b>	<b>97.0</b>

## Notes, Issues, Concerns

### 1. Ceiling Grid Install



### 2. HVAC Duct Work

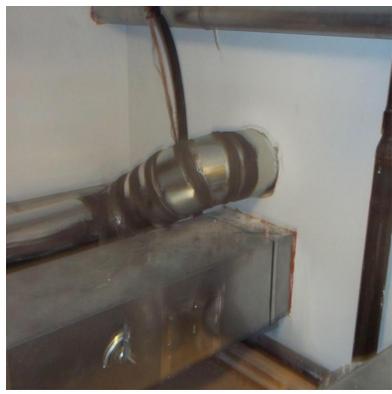

### 3. Wood Trim



### Site Safety Observations

No entry

### Quality Control Observations

No entry

### Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Lead Time on Specialty Light Fixtures. Nicore gas - Supply Natural Gas For Generator.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Board room & Community Rooms - SIPS Panel Roof
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Pole Braces to support Precast floor - Scissors Lift Painting Contractor

DBA

---

I, Dave Bender, verify this report is accurate and complete.
