


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 06/07/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:57°F Partly Cloudy



Wind: 4 MPH NW
Precipitation: .0"
Humidity: 79%

12:00 PM:66°F Mostly Cloudy



Wind: 9 MPH NW
Precipitation: .0"
Humidity: 58%

4:00 PM:73°F Mostly Cloudy




Wind: 8 MPH NW
Precipitation: .0"
Humidity: 49%

Work Logs

Name	Description	Quantity	Hours
Classic Touch Painting	Prep, Prime, Paint, - Wall Paper Install	3	8.0
Dumex Construction	2 - Working On Main Entrance Lobby Soffit 1- Install Ceiling Tile Borders.	3	10.0
Heartland Cabinetry	Install Wood Trim Cabinet install	2	8.0
Midwest Mechanical	Install HVAC Duct Work.	2	8.0
Superior Labor	Job site Clean Up, Misc Tasks.	1	8.0
Troop Contracting	Job Site Supervision	1	10.0
Valley Fire Protection	Fire Suppression Install.	2	8.0
Total		14	120.0

Notes, Issues, Concerns

1. Millwork - Podium For Dias - Coming Soon

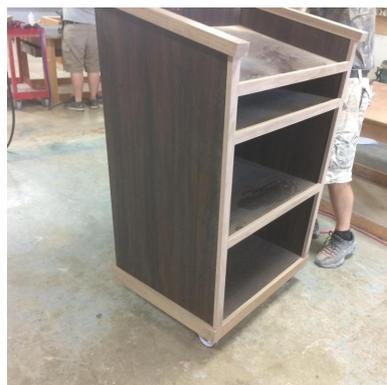


2. Cabinet Install



3. Main Entrance Lobby Soffit Install



4. Ceiling Tile Install

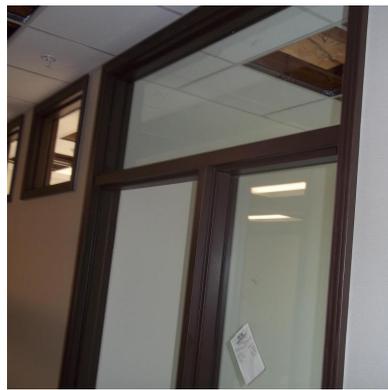

5. Fire Suppression Install



6. Concrete Infill



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

I, Dave Bender, verify this report is accurate and complete.
