


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Thu 06/09/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:58°F Mostly Cloudy



Wind: 5 MPH SE
Precipitation: .0"
Humidity: 73%

12:00 PM:72°F Light Rain



Wind: 8 MPH SW
Precipitation: .05"
Humidity: 61%

4:00 PM:81°F Mostly Cloudy




Wind: 10 MPH S
Precipitation: .0"
Humidity: 55%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Install Lighting - Trim outlets / Devices	2	8.0
Classic Touch Painting	Prime, Paint, & Wall Paper	4	8.0
Dumex Construction	2 Carpenters - install doors & Hardware. 2-drywall ceiling Sheriff's offices.	4	10.0
e.Norman Security	Install Security devices	1	8.0
Heartland Cabinetry	Millwork Install	2	8.0
Superior Flooring	Flooring Install	2	8.0
Superior Labor	Job site Clean up	1	8.0
Troop Contracting	Job site Supervision	1	10.0
Valley Fire Protection	Hydro Test Fire Supression System	2	8.0
Total		19	162.0

Notes, Issues, Concerns

1. Mill Work Install

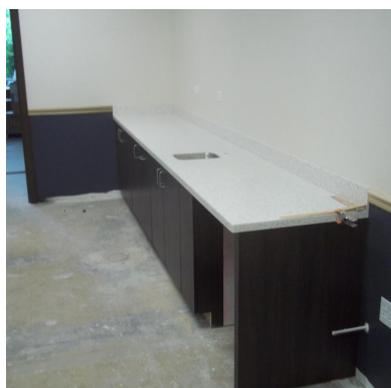

2. Door, & Hardware Install



3. Floor Install



4. Light Fixture Install



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A

Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Fire Inspector - Hydro Test on Fire Sprinkler system
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor
