


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Mon 06/13/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**55°F Clear



**Wind:** 3 MPH SE  
**Precipitation:** .0"  
**Humidity:** 76%

**12:00 PM:**79°F Clear



**Wind:** 5 MPH SW  
**Precipitation:** .0"  
**Humidity:** 42%

**4:00 PM:**88°F Partly Cloudy



**Wind:** 3 MPH SW  
**Precipitation:** .0"  
**Humidity:** 42%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric work	1	8.0
Classic Touch Painting	Prep, Prime, Paint, & Wall Paper Install	3	8.0
Dumex Construction	Carpentry - Install Lock sets & Hardware. Drywall Taping at Sheriff's Dept.	5	8.0
e.Norman Security	Installation of Security System	2	8.0
Heartland Cabinetry	Install Mock-up of wood wraps at Steel in Board Room	1	8.0
Midwest Mechanical	1 Sheet Metal - trim Defusers In ceilings. 1 Pipe fitter - Piped in EM Generator	2	8.0
Quinlan Security	Fire Alarm Work	2	6.0
Stutz Plumbing	Rod & Video Sanitary Mains. Trim Break Room & Coffee Bar Sinks.	2	8.0
Superior Flooring	Install Carpet Tiles	3	8.0
Superior Labor	General Clean Up	1	8.0
Troop Contracting	Jobsite Supervision	1	10.0
<b>Total</b>		<b>23</b>	<b>182.0</b>

## Notes, Issues, Concerns


1. Exterior Window Trimed



2. Steel Mock- Up



3. Sinks Trimed

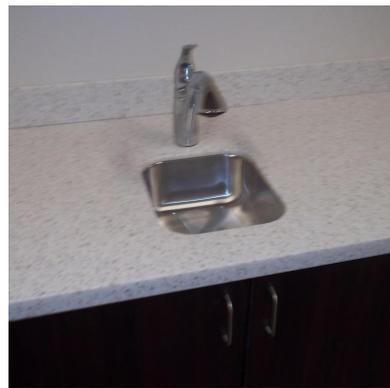

4. Carpet Install



5. Gas Pipe Tie In for Generator



6. Rod & Video Sanitary Lines



**Site Safety Observations**

No entry

**Quality Control Observations**

No entry

**Survey**

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village of Homer Glenn Building Department - Above Ceiling Inspection
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

DBE

---

I, Dave Bender, have reviewed and completed this report.
