


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Fri 06/17/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:61°F Clear



Wind: 4 MPH N
Precipitation: .0"
Humidity: 88%

12:00 PM:81°F Clear



Wind: 9 MPH NE
Precipitation: .0"
Humidity: 44%

4:00 PM:88°F Clear






Wind: 9 MPH NE
Precipitation: .0"
Humidity: 34%

Work Logs

Name	Description	Quantity	Hours
Action Caulking	Caulked 4 Doors & Thresholds	1	2.0
Arc Electric	Electric Trim & Install Base Board Heaters	1	8.0
Classic Touch Painting	Prime & Paint @ Sheriff's Dept Offices	1	8.0
Dumex Construction	2- Carpenters Door Hardware 2- carpenters SIPS Repair 2- Drywall Tapers	6	8.0
e.Norman Security	Security System install	1	6.0
Superior Flooring	Install Carpet & Base. Install under laymen Entrance Lobby	3	8.0
Superior Labor	General Construction Clean up	1	8.0
Troop Contracting	Job Site Supervision	1	10.0
Total		15	114.0

Notes, Issues, Concerns

1. Carpet Install

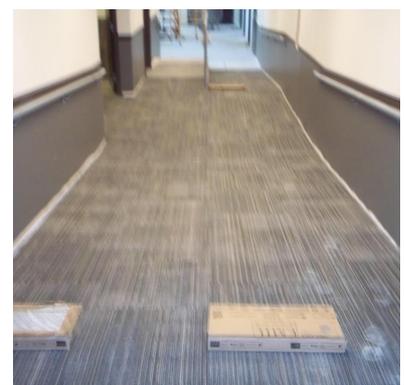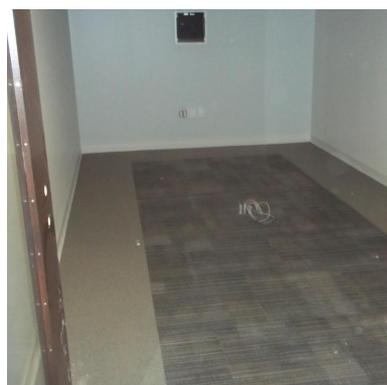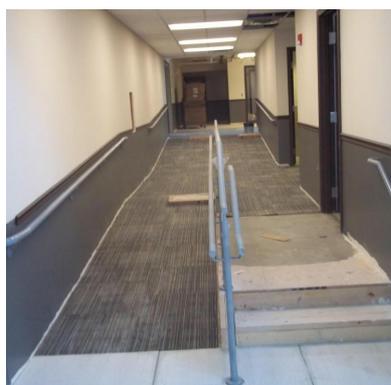

2. Doors & Thresholds Caulked



3. Door Locks Installed



4. Canopy Coating



5. SIPS Panel / Roof Work



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village of Homer Glen, Chief Building Official, Joseph Baber
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



I, Dave Bender, have reviewed and completed this report.
