


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Thu 06/30/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**58°F Clear



**Wind:** 2 MPH S  
**Precipitation:** .0"  
**Humidity:** 81%

**12:00 PM:**77°F Clear



**Wind:** 6 MPH S  
**Precipitation:** .0"  
**Humidity:** 45%

**4:00 PM:**84°F Partly Cloudy



**Wind:** 8 MPH SW  
**Precipitation:** .0"  
**Humidity:** 43%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Trim & Work with Security Contractor	1	4.0
Classic Touch Painting	Stain Wood beams in Community Room	1	8.0
Des plaines glass	Install New Exterior Doors & Frames	1	8.0
Dumex Construction	Install Door hardware	2	8.0
e.Norman Security	Completing Install of Security system	1	8.0
Furniture Installers	Install New Office Furniture & Conference Room Tables	5	8.0
Heartland Cabinetry	Install Barn Door Track & Finish work on Main reception Desk	1	8.0
Quinlan Security	Survey Existing Fire Alarm Devices.* 2- devices replaced in High ceiling Building Dept open office Area.	1	8.0
Superior Flooring	Install Floor Sheriff's Kitchen & back landing. Float / Skim coat main Entrance Lobby floor	2	8.0
Superior Labor	General labor & Clean up.	1	8.0
Troop Contracting	Job Site Supervision	1	12.0
<b>Total</b>		<b>17</b>	<b>136.0</b>

## Notes, Issues, Concerns


1. New Office Furniture & Conference Room Tables



2. Beams Stained



3. Barn Door Track & Feature Wall

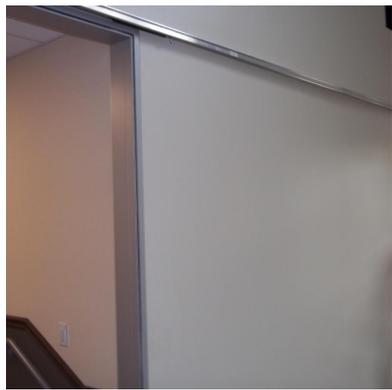

4. Main reception Desk



5. Floor Install Sheriff's Dept



### Site Safety Observations

---

No entry

### Quality Control Observations

---

No entry

### Survey

---

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

---

I, Dave Bender, have reviewed and completed this report.
