


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 07/05/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:68°F Mostly Cloudy



Wind: 1 MPH SW
Precipitation: .0"
Humidity: 92%

12:00 PM:77°F Mostly Cloudy



Wind: 6 MPH SW
Precipitation: .0"
Humidity: 73%

4:00 PM:83°F Mostly Cloudy



Wind: 8 MPH SW
Precipitation: .0"
Humidity: 62%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric work	2	8.0
Classic Touch Painting	Paint Windows & stain wood beams in Community room	3	8.0
Dumex Construction	Finish Door Hardware install, Install ceiling tiles lobby 163	2	8.0
e.Norman Security	Install Security System	1	8.0
Heartland Cabinetry	Fur out steel beams to receive wood wraps	3	8.0
Superior Flooring	Install LVT tile in lobby	2	8.0
Superior Labor	General Labor & Clean up	1	8.0
Troop Contracting	Job Site Supervision	1	8.0
Valley Fire Protection	Install Fire suppression	2	8.0
Total		17	136.0

Notes, Issues, Concerns

1. LVT Tile Install




2. Furring for Steel Beam Wood Wrap



3. Window Painting



4. Beam Staining

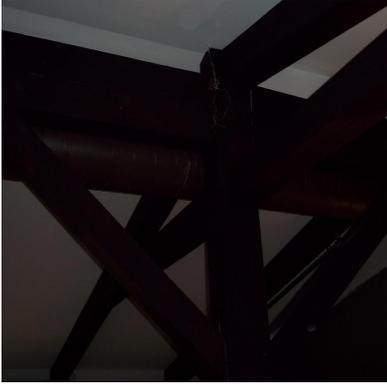

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A

Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village of Homer Glen, Chief Building Official, Joseph Baber. Village of Homer Glen John Robinson
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



I, Dave Bender, have reviewed and completed this report.
