


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Thu 07/07/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:69°F Clear



Wind: 4 MPH SW
Precipitation: .0"
Humidity: 92%

12:00 PM:80°F Partly Cloudy



Wind: 4 MPH S
Precipitation: .0"
Humidity: 72%

4:00 PM:82°F Light Rain



Wind: 4 MPH S
Precipitation: .04"
Humidity: 74%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Trim. Install Can Light in Board Room	1	10.0
B & H Brickwork	Tuck point / infill around Fire Connection	1	1.0
Classic Touch Painting	Stain Wood Beams Board & Community Rooms	1	8.0
Des Plaines Glass	Finish Hardware Install on Fiberglass doors	1	8.0
Dumex Construction	2- Tapers- working in Board & Community Rooms. 1- Carpenter Misc tasks	3	8.0
e.Norman Security	Install Security System	1	4.0
Heartland Cabinetry	Wood Wrap Steel Beams	2	8.0
J.L. Door	Install Overhead Electric Door Strikes Main Entrance Doors	1	4.0
Quinlan Security	Fire Alarm Test	2	4.0
Superior Flooring	1- Installed rubber stair risers. 3- skim coat Community room Floor -2nd shift	4	8.0
Superior Labor	General Labor & Clean up	1	8.0
Team Logic IT	Phone & Data Install	2	8.0
Troop Contracting	Job Site Supervision	1	12.0
Valley Fire Protection	Fire Sprinkler Test	2	8.0
Total		23	167.0

Notes, Issues, Concerns


1. Wood Wraps



2. Wood Beams Stained



3. Rubber stair treads & Risers

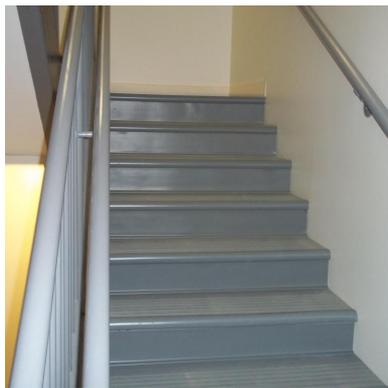

4. Fiberglass Exterior Doors



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village of Homer Glen, Chief Building Official, Joseph Baber & Homer Township Fire Protection, Deputy Fire Marshal, Dave Bricker.
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



I, Dave Bender, have reviewed and completed this report.
