


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Date** Tue 07/12/2016

**Job #** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**72°F Partly Cloudy



**Wind:** 6 MPH S

**Precipitation:** .0"

**Humidity:** 90%

**12:00 PM:**86°F Partly Cloudy



**Wind:** 8 MPH S

**Precipitation:** .0"

**Humidity:** 69%

**4:00 PM:**87°F Drizzle



**Wind:** 10 MPH SW

**Precipitation:** .01"



**Humidity:** 61%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough in conduit for lighting Board & Community Rooms	1	12.0
Classic Touch Painting	Stain Wood Beams & Wood Beam Wraps	1	8.0
Dumex Construction	1- Carpenter Misc tasks 2- drywall tapers	3	8.0
e.Norman Security	Programing- testing card readers for security system	2	8.0
Heartland Cabinetry	Install Beam wraps	2	8.0
Midwest Mechanical	Finish install Spiral duct work	1	3.0
Superior Labor	General Labor & Clean up	1	8.0
Troop Contracting	Job Site Supervision	1	9.0
<b>Total</b>		<b>12</b>	<b>96.0</b>

## Notes, Issues, Concerns

### 1. F-12 Wall Sconces Installed

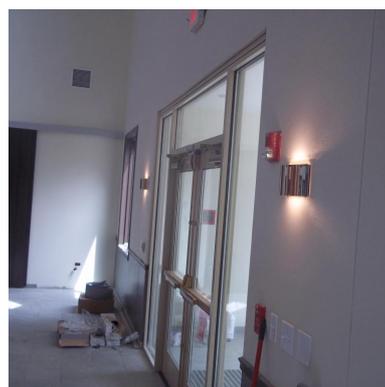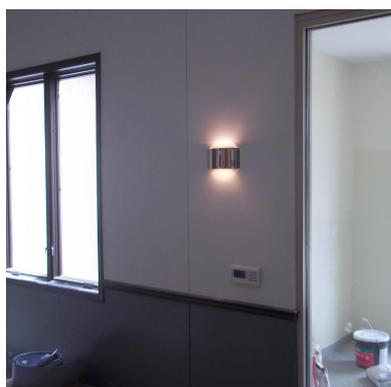

### 2. Wood Beams & Wraps stained



3. Misc Photos



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

I, Dave Bender, have reviewed and completed this report.
