


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Thu 07/14/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:69°F Overcast



Wind: 4 MPH SW
Precipitation: .0"
Humidity: 93%

12:00 PM:80°F Partly Cloudy



Wind: 10 MPH SW
Precipitation: .0"
Humidity: 67%

4:00 PM:86°F Clear




Wind: 17 MPH W
Precipitation: .0"
Humidity: 42%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	1- AM - Install lights in Sheriff's Department. 5 - PM install boxes & Conduit for lights @ Board & Community Rooms	1	12.0
Classic Touch Painting	Stain wood beams & Wood beam wraps	2	8.0
e.Norman Security	Programing Security System	1	8.0
Heartland Cabinetry	Install Stationary Panel next to Barn door. Chair rail install Board & Community Rooms	2	8.0
Superior Flooring	Start Ceramic tile Re-work, Entrance Lobby	2	8.0
Superior Labor	General Labor & Clean up	1	8.0
Troop Contracting	Job Site Supervision	1	11.0
Total		10	87.0

Notes, Issues, Concerns


1. Village of Homer Glen Move in Day



2. Move In Day



3. Wood Beams Stain

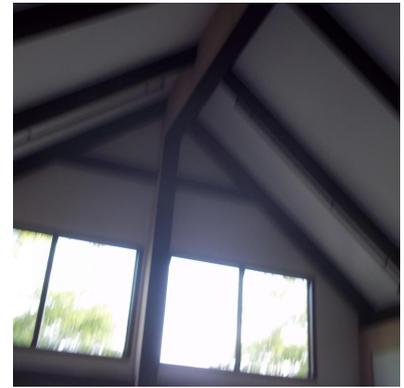

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor

DS

I, Dave Bender, have reviewed and completed this report.
