


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Fri 07/15/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:64°F Mostly Cloudy



Wind: 3 MPH W
Precipitation: .0"
Humidity: 86%

12:00 PM:74°F Mostly Cloudy



Wind: 7 MPH W
Precipitation: .0"
Humidity: 67%

4:00 PM:74°F Light Rain




Wind: 3 MPH NW
Precipitation: .02"
Humidity: 72%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Install Lighting Building Dept - Axis Pendent	3	12.0
Classic Touch Painting	Paint & Stain In Board Room	2	8.0
Des plaines glass	Replace Broken pane of Glass	1	2.0
e.Norman Security	Install & Program Security System	1	8.0
Heartland Cabinetry	Install DAIS Base Cabinets in Board Room	3	10.0
Superior Flooring	Install Flooring	6	8.0
Troop Contracting	Job Site Supervision	1	14.0
Total		17	154.0

Notes, Issues, Concerns

1. Axis Pendent light install

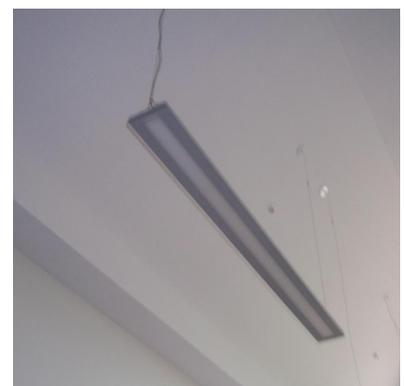

2. Signage Install



3. Wood Beams Stained



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A

DB

I, Dave Bender, have reviewed and completed this report.
