


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Wed 07/20/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:70°F Partly Cloudy



Wind: 2 MPH SE
Precipitation: .0"
Humidity: 91%

12:00 PM:86°F Mostly Cloudy



Wind: 7 MPH S
Precipitation: .0"
Humidity: 63%

4:00 PM:87°F Partly Cloudy




Wind: 5 MPH SW
Precipitation: .0"
Humidity: 57%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Installing Conduit for Pendent lights in Board & Community rooms. install conduit for A/V Contractor. pull wire for outlets in Dais Desk.	1	10.0
Classic Touch Painting	Paint Conduits attached to beams and ceilings in Board & Community Rooms	1	8.0
Pace Systems	Install cable in Dais Desk. run speaker wire for speakers.	2	8.0
Troop Contracting	Job Site Supervision	1	11.0
Total		5	45.0

Notes, Issues, Concerns

1. Install Low Voltage Wiring & Power into Dais Desk

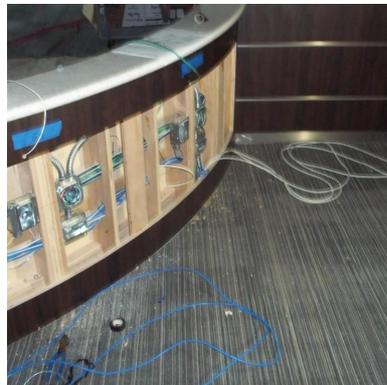

2. Counter Top Install for Dais Desk



3. Conduit & Lighting for Board & Community Rooms



Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	Weekly OAC Meeting
Any areas that can't be worked on?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any equipment rented on site?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A

DBI

I, Dave Bender, have reviewed and completed this report.
