


# Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



**Report Date** 04/20/2016

**Job Number** 16-012

**Prepared By** Dave Bender

## Weather

**6:00 AM:**52°F Clear



**Wind:** 7 MPH E  
**Precipitation:** .0"  
**Humidity:** 57%

**12:00 PM:**68°F Mostly Cloudy



**Wind:** 9 MPH SE  
**Precipitation:** .0"  
**Humidity:** 47%

**4:00 PM:**74°F Overcast




**Wind:** 10 MPH SE  
**Precipitation:** .0"  
**Humidity:** 47%

## Work Logs

Name	Description	Quantity	Hours
Arc Electric	Security Rough in	2	8.0
Midwest Mechanical	Set up for New Gas Pipe Install	1	8.0
Troop Contracting	Job Site Supervision. Meetings - SIPS Panels. Fire Marshal, fire Sprinkler, fire alarm Contractors. Owner, Architect, Contractor Meeting.	1	12.0
<b>Total</b>		<b>4</b>	<b>36.0</b>

## Notes, Issues, Concerns

1. Electric rough in

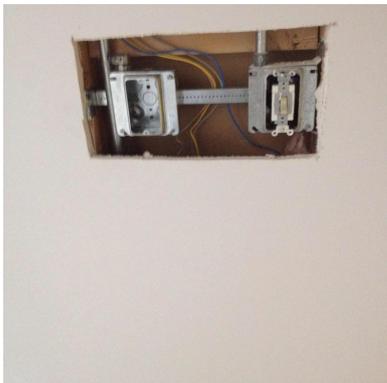

## Site Safety Observations

No entry

## Quality Control Observations

No entry

## Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Approved Submittals - Long lead items & Material. - SIPS panels Issues - HVAC RFI Responses.
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Meeting - SIPS, Village of Homer Glen, Tria Architecture, Troop Contracting, Energy Building Systems. Meeting- Homer Township Fire Marshal, Village of Homer Glen, Troop Contracting, Valley Fire Protection, Quinlin Security Systems. Meeting- OAC, Village of Homer Glen, Tria Architecture, KGZ Engineering, Troop Contracting.
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC Contractor - * In Review of Architect, MEP Engineers, Comments on Outstanding RFI's.
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



---

I, Dave Bender, verify this report is accurate and complete.
