


Homer Glen Village Hall Renovations

14240 W. 151 ST Homer Glen, IL 60491



Date Tue 05/03/2016

Job # 16-012

Prepared By Dave Bender

Weather

6:00 AM:39°F Clear



Wind: 3 MPH W
Precipitation: .0"
Humidity: 86%

12:00 PM:64°F Clear



Wind: 7 MPH W
Precipitation: .0"
Humidity: 41%

4:00 PM:65°F Partly Cloudy




Wind: 10 MPH W
Precipitation: .0"
Humidity: 36%

Work Logs

Name	Description	Quantity	Hours
Arc Electric	Electric Rough in for Lighting	2	8.0
Dumex Construction	Hollow Metal Door & Frame Install	2	8.0
Midwest Mechanical	Condensation Drain Install for Split System IT Room 006. T-Stat location - Install.	2	8.0
Stutz Plumbing	Complete wall rough - pass rough inspection.	2	4.0
Troop Contracting	Jobsite Supervision	1	8.0
Total		9	64.0

Notes, Issues, Concerns

1. Electric rough in Lighting

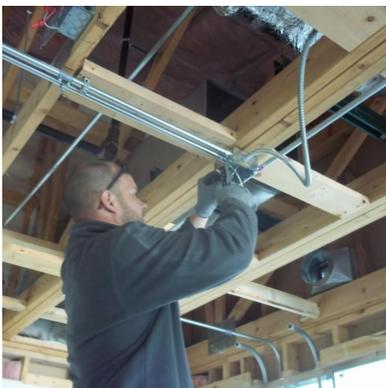

2. Hollow Metal Door & Window Install




3. Wood Backing Install for video monitors



4. Copper water lines re-worked, interview room 162



5. IT Room Split Cooling Unit, Condensation line installed

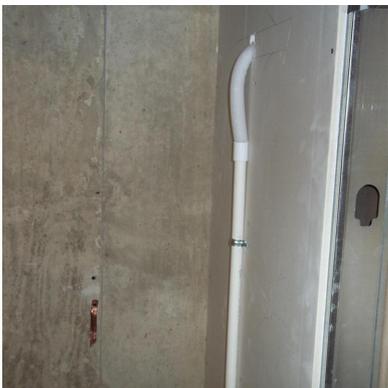

Site Safety Observations

No entry

Quality Control Observations

No entry

Survey

	No	Yes	Description
Any accidents on site today?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Hot issues that may effect schedule?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	MSK's on HVAC RFI's. SIPS Panel Roof & Wall Leaks, - Answers / responses, on Issues, From Both Architect & Owner (* Causing Major Delays in Construction activities*)
Did weather cause any delays?	<input checked="" type="checkbox"/>	<input type="checkbox"/>	N/A
Any visitors on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Village Homer Glen, John Robinson, Walk thru with A Team Logic It - Company to install Data & voice cable.
Any areas that can't be worked on?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	HVAC - Duct Work- SIPS Panels -Board Room
Any equipment rented on site?	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Pole Braces to support Precast floor



I, Dave Bender, verify this report is accurate and complete.
